ROLE BRIEF · RESTAURANT BILLING SAAS



Sous Chef

Aditya

Frontend & UI Developer · light backend

Every role gets a fast, obvious screen. A cashier closes a bill in under 30 seconds; a waiter punches an order one-handed on a phone.

SERVICE WINDOW	PLATES	FINAL TASTING
13 Oct – 1 Nov 2026	Standard · Pro · Premium	AC-01 to AC-12

Works with **Gagan** · Head Chef (Full Stack + DevOps)
Companion to **The Kitchen Playbook**

BASED ON SRS V1.0 · PREPARED 12 OCTOBER 2026

COURSE ONE

01 Your Role: Sous Chef

You own everything the guest and staff see: every screen on Windows, Android and the web admin portal, the design system, and the user guides. You also build simple CRUD endpoints following Gagan's pattern, under his review.

REPORTS TO	WORKS WITH	TIME SPLIT
Gagan, Head Chef	Gagan on every API contract	85 screens / 10 backend / 5 docs

Mission. Every role gets a fast, obvious screen. A cashier closes a bill in under 30 seconds; a waiter punches an order one-handed on a phone.

What good looks like on 1 Nov

Bill closed in under 30 s
from table tap to printed receipt

Waiter order one-handed
on a phone, large touch targets

Every screen has 3 states
loading, empty and error

Never blocked on an API
build on mocks, swap when staging lands

Same look on all devices
everything comes from ui_kit tokens

User guides by Day 19
one per role, with screenshots

Your decision rights: Layout, interaction, visual design and component API. You raise an API change request rather than working around the contract.

Daily capacity



85% screens · 10% light backend · 5% docs

COURSE TWO

02 What You Own

> Everything below is yours to build and answer for. Items marked as review are checked by Gagan before they merge.

Design system "House Plating"

- Restaurant palette, typography, spacing and tokens in `packages/ui_kit`
- Components: buttons, numeric keypad, dialogs, table tiles, order cards, status chips, offline banner
- Screen map (handoff deliverable, Day 2) and wireframes for every role

Super Admin web portal (Flutter Web)

- Restaurant list with search and filters (status, plan, license expiry, owner)
- Onboarding form, activate / block / suspend actions with reason
- License screens, platform admins and roles, MFA enrol / step-up / reset, audit viewer

POS app (Flutter, Windows + Android)

- Login and role-based routing: cashier, waiter, chef, owner, IT admin, auditor
- Table map with floors, dine-in and takeaway order taking, menu management + image upload
- Bill, payment (cash / UPI / card, across modes), tip-to-waiter, discount and reversal dialogs
- Bill history, reprint, receipt layout; hub pairing screen; sync status indicator
- Waiter mode on Android: assigned tables, order entry, modifications, status

Premium screens

- Kitchen Display: ticket queue, accept / preparing / ready, timers
- Recipe editor, menu approval inbox, publish flow
- Inventory: stock list, receipts, transfers, wastage, low-stock alerts
- Shifts and breaks; owner and franchise dashboards; reports; franchise invoice PDF layout

Light backend & docs

- Menu, category, table and floor CRUD endpoints in NestJS, copying Gagan's module pattern
- Seed and demo data
- User guides with screenshots for cashier, waiter, chef, owner, IT admin and auditor
- UI tests of the happy path for each screen; review Gagan's UI PRs

COURSE THREE

03 Your Stations (RACI)

> 19 of 24 modules need work from you. A = you answer for it, R = you do the work; Gagan's part is shown so you know who to talk to.

Module	You	Gagan	Done by
Screen map + design system	**A/R**	C	Day 2
Tenant onboarding, restaurant lifecycle	**R portal UI**	A/R backend	Day 3
Auth, RBAC, platform admins, MFA + step-up reset	**R screens**	A/R	Day 4
Licensing, plans, entitlements	**R screens**	A/R	Day 4
Audit & security logs	**R viewer**	A/R	Day 4
Menu, categories, tax rules, images	**R (CRUD + UI)**	A, review	Day 6

Module	You	Gagan	Done by
Tables, floors, table transfer	**R CRUD + layout UI**	A/R transfer logic	Day 9 / 11
Orders, bills, taxes, tips, discounts, reversals	**R screens**	A/R	Day 9
Printing	**R receipt layout**	A/R driver	Day 9
Waiter Android mode	**A/R**	C	Day 13
Local LAN hub, pairing, offline queue, cloud sync	**R status UX**	A/R	Day 13
Franchise/branches, branch-scoped RBAC, auditor	**R dashboards**	A/R	Day 14
Kitchen Display System	**A/R screens**	R events	Day 15
Recipes + menu approval workflow	**R screens**	A/R	Day 15
Inventory + stock lifecycle	**R screens**	A/R	Day 16
Shifts, breaks, attendance	**A/R**	R	Day 17
Consolidated franchise invoice	**R PDF layout**	A/R	Day 17
Reports & dashboards	**A/R**	R queries	Day 17
User docs + admin ops guide	**A/R user docs**	A/R ops guide	Day 19

COURSE FOUR

04 Your 20-Day Service

> One row per day, 13 Oct to 1 Nov 2026. Tick each row at the 20:00 Closing Check. Shaded rows are client tastings.

Day	Date	Your tasks	Needs from Gagan	Tasting / gate	Done
1	Tue 13 Oct	Design system tokens + restaurant palette; screen map; POS wireframes	Nothing: design work only	Defaults sent to client	☐
2	Wed 14 Oct	ui_kit components (buttons, keypad, dialogs, table tile, order card); login screens; portal shell	Login / auth contract + mocks	Handoff pack to client; defaults signed	☐
3	Thu 15 Oct	Portal: restaurant list/search/filter, onboarding form, status actions	Tenant + onboarding contract		☐
4	Fri 16 Oct	Portal: license screens, admin users & roles, MFA enrol/reset, audit viewer	License, admin-roles, MFA, audit contracts		☐
5	Sat 17 Oct	POS app shell, role-based routing, hub pairing screen; menu screens on mocks	Pairing API + WebSocket spec	**Course 1: AC-01, 02, 03 demo**	☐
6	Sun 18 Oct	Menu/category/table CRUD endpoints (light backend); menu management + image upload UI	CRUD module pattern; image upload endpoint		☐
7	Mon 19 Oct	Table map (free/occupied), dine-in + takeaway order screen	Order engine contract + table events		☐
8	Tue 20 Oct	Bill screen, payment dialog (cash/UPI/card, pay across modes), tip selector, reversal dialog	Bill / payment / tip / reversal contracts		☐
9	Wed 21 Oct	Receipt layout, table transfer UX, bill history + reprint	Transfer endpoint; print API		☐
10	Thu 22 Oct	Sync status indicator, offline banner, Standard end-to-end polish	Sync status API	**Course 2: Standard MVP, AC-04 to 06; build sent**	☐

Day	Date	Your tasks	Needs from Gagan	Tasting / gate	Done
11	Fri 23 Oct	Floor layout editor, floor switcher, cross-floor transfer	Floor model + concurrency events		☐
12	Sat 24 Oct	Waiter mode (Android): assigned tables, order entry, modifications	Waiter-scoped order APIs		☐
13	Sun 25 Oct	Waiter order status, connection states, error/empty states	Connection-state events	**Course 3: Professional, AC-07, 08**	☐
14	Mon 26 Oct	KDS screens: ticket queue, accept/preparing/ready, timers	KDS ticket event spec		☐
15	Tue 27 Oct	Recipe editor, approval inbox, publish flow	Recipe + approval API		☐
16	Wed 28 Oct	Inventory screens: stock list, receipt entry, transfer, wastage, low-stock alerts	Inventory API		☐
17	Thu 29 Oct	Shift + break screens, owner + franchise dashboards, reports	Shift API, report queries, invoice data	**Course 4: Premium, AC-09 to 12**	☐
18	Fri 30 Oct	UI polish, tablet layouts, accessibility, bug-bash fixes	Bug list from security pass	Release candidate rc1	☐
19	Sat 31 Oct	User guide with screenshots, demo data, client UAT support	Production builds to screenshot	**Client UAT on production**	☐
20	Sun 1 Nov	UAT fixes, final screen walkthrough	UAT fix list	**Sign-off + final invoice**	☐

Buffer: Mon 2 Nov to Sat 7 Nov for slips and client-requested fixes. Cut line: if Course 3 is not green by Sun 25 Oct, Premium drops to the reduced scope in the main playbook.

COURSE FIVE

05 Your Quality Checks at the Pass

> You own 3 of the 12 acceptance criteria the client signs before paying the balance. Each needs a passing test and a live demo on its day.

AC	Workflow	Demo day	What your screens must show
AC-06	Tip attribution	10	Tip selector with waiter picker; dine-in tip without waiter prompts
AC-09	KDS	17	KDS queue, status buttons, timers; status chips on waiter/cashier
AC-12	Franchise invoice	17	Invoice PDF layout with branch breakdown

Screens that support Gagan's criteria

Gagan owns the logic for these, but the demo runs through your screens, so they must show the right state:

AC	Workflow	Demo day	What your screens must show
AC-02	License enforcement	5	License-expired and blocked banners; disabled actions
AC-03	MFA reset	5	MFA enrol, step-up prompt and reset screens
AC-04	Table transfer	10	Transfer picker shows occupied tables and conflict message
AC-05	Item reversal	10	Reversal dialog makes reason mandatory; totals refresh
AC-07	Concurrent cashiers	13	Pay button disables while pending; one success toast
AC-08	Offline LAN	13	Offline banner and pending-sync count visible
AC-11	Auditor	17	Read-only auditor views with no edit controls

COURSE SIX

06 Working with Gagan

1. Each day at 12:00 Gagan drops tomorrow's API contract + mock JSON. Start screens on the mocks (Needs from Gagan column below).
2. When a real endpoint lands on staging, switch the screen over the same day and tell Gagan if anything differs from the contract.
3. Need a field or endpoint changed? Open a PR to `packages/contracts` and tag Gagan; do not work around it in the UI.
4. Your CRUD endpoints (menu, category, table, floor) copy Gagan's module pattern and always go through his review.
5. A bug you are unsure about: post it with steps and a screenshot; Gagan triages within 2 hours.

Daily rhythm

Time (IST)	Ritual	What you do
10:00	Morning Briefing (15 min)	Yesterday done, today's plate, blockers
12:00	Contract drop	Pick up tomorrow's contract + mocks from Gagan
18:30	Staging tasting	Check today's screens on Windows, Android and web


Time (IST)	Ritual	What you do
20:00	Closing Check	Push, update the board, tick today's row

Definition of done: merged to `main`; on staging; happy-path and one failure-path test pass; critical actions have audit + permission checks; screens have loading, empty and error states; board card moved to Done.

COURSE SEVEN

07 Your Kitchen and Tools

Gagan builds what sits behind your screens. What matters for the UI: every device talks to the branch hub, so your screens must show hub and sync status clearly, and keep working when the internet is down.

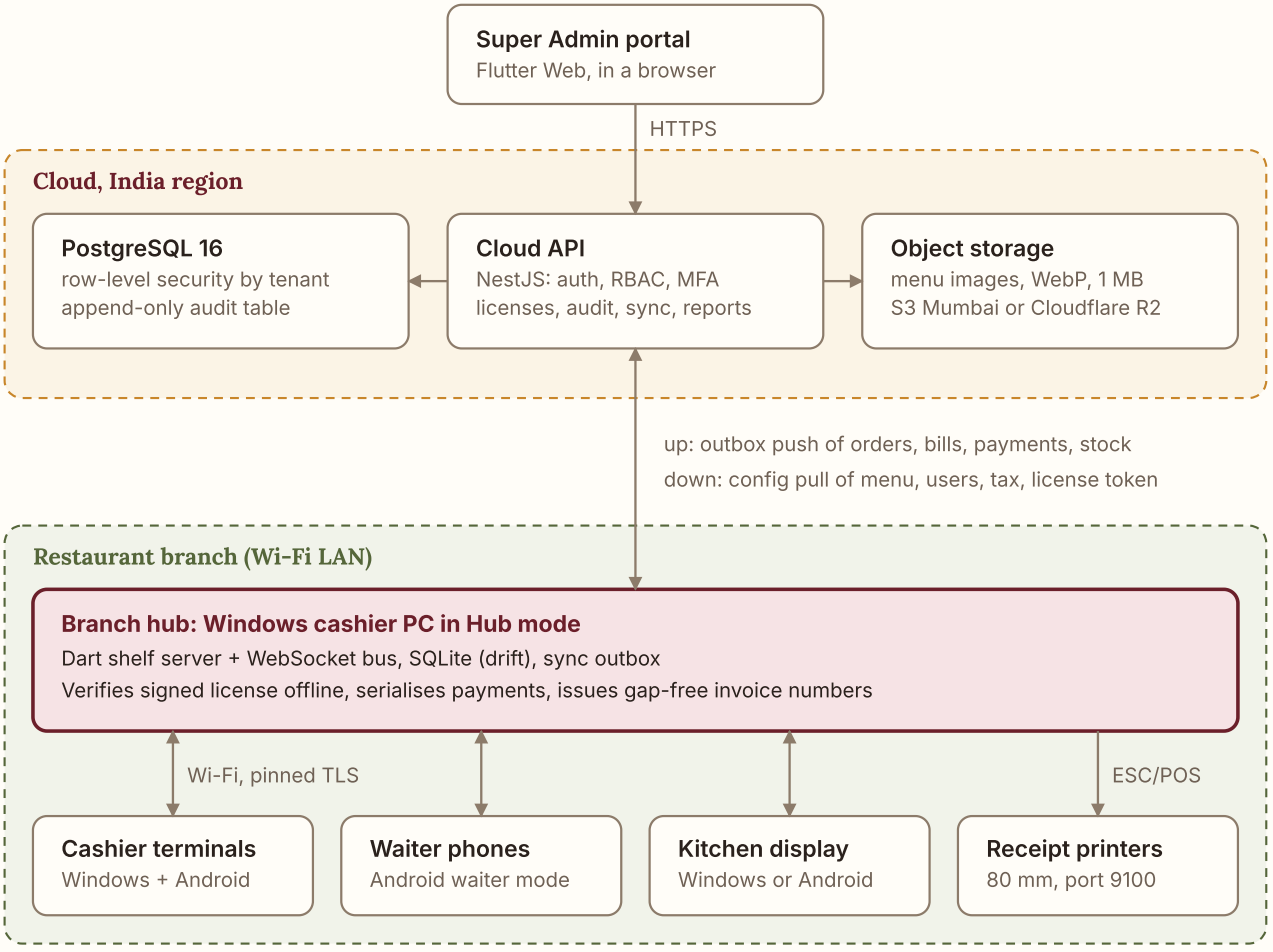

Branch devices talk to the hub; only the hub talks to the cloud. If the hub is switched off, the branch pauses rather than splitting into two versions of the truth.

Your stack

Layer	Choice	Why it fits 20 days	Owner
POS / waiter / KDS app	Flutter 3 (Windows + Android), Riverpod, go_router	One codebase, both target OSes, team already fluent	Aditya
Super Admin portal	Flutter Web (separate app, shared UI kit)	Same components + same stack; SRS allows a browser portal	Aditya

Layer	Choice	Why it fits 20 days	Owner
Cloud API	NestJS (TypeScript) + Prisma	Fast CRUD, guards for RBAC/entitlements, OpenAPI generation	Gagan (Aditya: simple CRUD)
Printing	ESC/POS over TCP 9100 (80 mm thermal) + Windows PDF / system print fallback	Works on both OSes without vendor SDKs	Gagan + Aditya
PDFs	`pdf` Dart package (receipts, franchise invoice)	Same layout on all devices	Aditya
Testing	Jest + Supertest (API), Dart `test` (core/hub), Flutter widget + integration tests, k6 (load)	Covers SRS §9 automated test list	Both

COURSE EIGHT

08 Your Kitchen Fires

Risk	Likelihood	What you do about it
Waiting on a backend endpoint	High	Build on the mock JSON from `packages/contracts`; swap to staging when it lands
Screens differ between Windows and Android	Medium	All sizes and colors from ui_kit tokens; check every screen on both by 18:30 staging tasting
Too many Premium screens in week 3	High	Reuse list/detail/form templates from the portal; follow the cut line if Course 3 slips
Printer receipt looks wrong on paper	Medium	Lay out at 80 mm (48 characters per line); test on the client's printer by Day 9
Polish eats feature time	Medium	Polish only on Day 18; before that, functional plus three states is done
Burnout	High	Take your half-day off Sat 24 Oct PM and one more in week 3

COURSE NINE

09 Your Closing Checklist

Before full build, Day 2

- [ ] Screen map for every role
- [ ] Design tokens + core components in ui_kit
- [ ] Wireframes for POS, waiter, KDS and portal

Handoff pack, Day 20

- [ ] All screens on Windows, Android and web build from `main`
- [ ] User guides with screenshots for every role
- [ ] Receipt and franchise invoice PDF layouts
- [ ] Demo data seeded for the final tasting
- [ ] UI happy-path tests green in CI

Aditya, Sous Chef · Signature & date

Gagan, Head Chef (Full Stack + DevOps) · Acknowledged
